

**COUNTY OF SAN MATEO****Inter-Departmental Correspondence****Date:** October 9, 2001**Board Meeting Date:** October 23, 2001

**To:** Honorable Board of Supervisors

**From:** Neil R. Cullen, Director of Public Works

**Subject:** **Pescadero Creek Road Slides Repair – Loma Mar Area  
Rescinding Board of Supervisors Resolution No. 64821**

**RECOMMENDATION**

Adopt a resolution rescinding Resolution No. 64821, which adopted plans and specifications and called for sealed proposals for Pescadero Creek Road Slides Repair.

**Previous Board Action**

Adopted Resolution No. 64821 on September 25, 2001, adopting plans and specifications, determining prevailing wage scales, and calling for sealed proposals for Pescadero Creek Road Slides Repair.

**Key Facts**

The proposed project will repair portions of the travel lane and shoulder on Pescadero Creek Road at two locations, which were undercut as a result of creek bank erosion or excessive ground water.

**Discussion**

On September 25, 2001 your Board adopted Resolution No. 64821 adopting plans and specifications for the repair of two slides on Pescadero Creek Road in the Loma Mar area. We mentioned in our report to your Board that we were seeking a renewal of the Department of Fish and Game (F&G) permit that is required for this work. Our request to F&G included an extension of the window in which work would be permitted, as it was our understanding the work on the proposed retaining walls could be done this winter since the proposed walls are not directly within the creek proper. We recently received the renewal of the permit with an expiration date of December 31, 2002. However, F&G restricted construction to the period between June 15th and October 15th. It is our understanding that we may request to do work past the October 15th cutoff date, but that F&G would only approve work on a day-to-day basis and the permit to work could be revoked at any time.

Honorable Board of Supervisors

**Subject: Pescadero Creek Road Slides Repair – Loma Mar Area  
Rescinding Board of Supervisors Resolution No. 64821**

October 9, 2001

**Board Meeting Date: October 23, 2001**

Page 2


Our initial intention was to award a contract this fall and have the contractor order the material and do the retaining wall work that is out of the creek proper, and then suspend the work until the spring. However, the latest restrictions in the F&G permit limits our ability to allow the contractor to do the work on the walls and subjects the County to additional claims if the project site changes, due to erosion or other natural phenomena, between the time the contractor bids the work and when he is allowed to do the actual construction. Therefore, we are returning to your Board with a recommendation to rescind the resolution calling for bids for this work and to re-advertise the work in the spring of 2002 when the work is allowed by the new timing requirements of the Department of Fish and Game.

In the interim, we will do what is necessary to keep the road open through this winter.

**Fiscal Impact**

The estimated total cost for construction for the two slide repairs is \$1,003,000. Funds for the work have been budgeted in this year's Road Fund Budget.

A form of resolution has been approved by County Counsel.

  
Neil R. Cullen  
Director of Public Works


NRC:BCL:BEK:RO:RKL:sdd

F:\USERS\ADMIN\ESD\Pescadero Creek Road\BOARDSUP\2001\Rescind-adoptres.doc  
F:\USERS\Rogroup\Richard\Pscslide\Board\Rescind-adoptres.DOC

**File No.: F-36 (354)**

Attachments: Vicinity and Location Maps

cc: Milt Mares, County Counsel  
Brian C. Lee, P.E., Division Manager, Programs and Engineering Services  
Bruce E. Kirk, Principal Civil Engineer, Project Development and Design

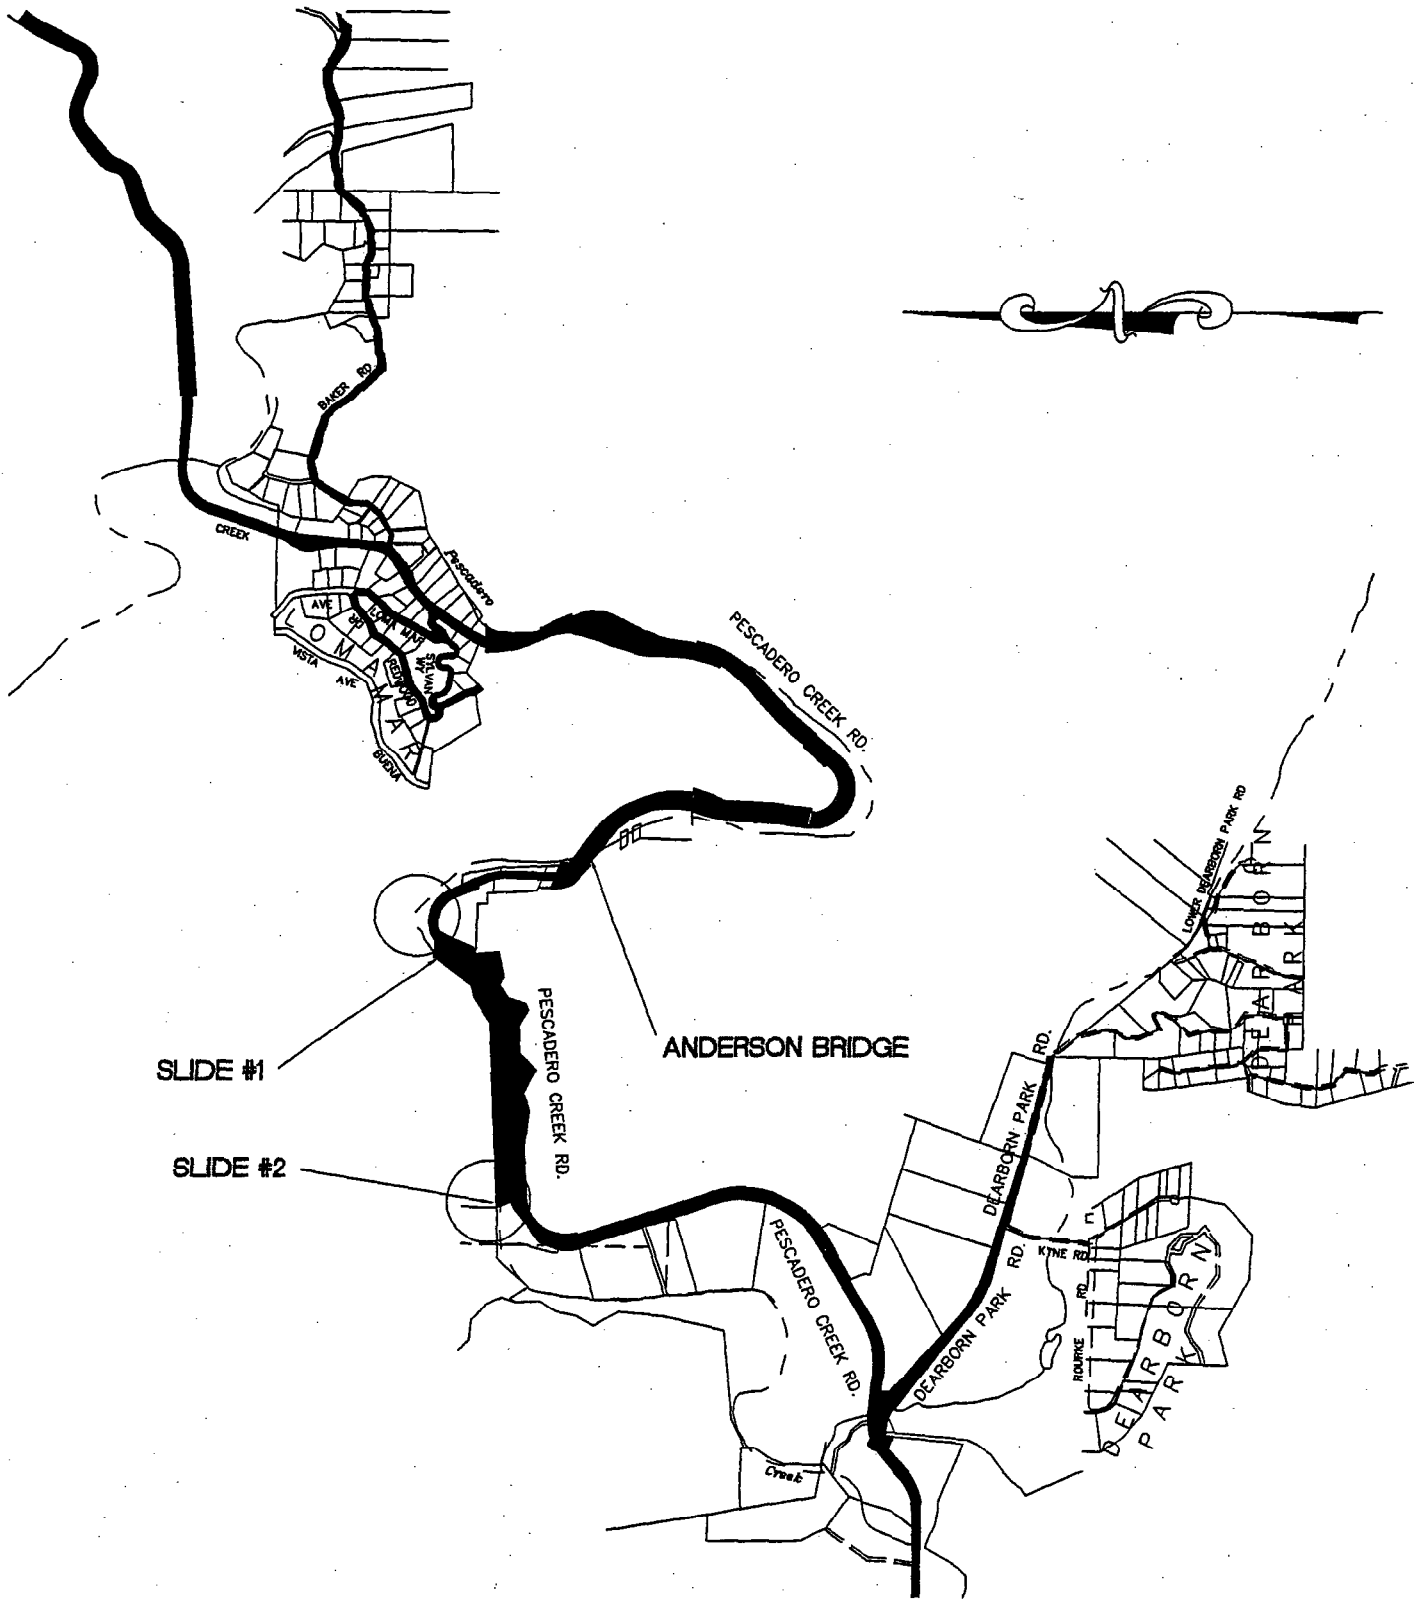

DESIGNED BY: RL

CHECKED BY: RD

DRAWN BY: RKL

PESCADERO CREEK ROAD SLIDES REPAIR PROJECT  
 IN LOMA MAR AREA OF SAN MATEO COUNTY  
**LOCATION MAP**  
**EXHIBIT 'A'**

SCALE: NONE

DATE: 7/1/01

FILE NO: E4558

NEIL R. CULLEN, DIRECTOR OF PUBLIC WORKS  
 SAN MATEO COUNTY

555 COUNTY CENTER, 5TH FLOOR  
 REDWOOD CITY, CALIFORNIA 94063-1665



Resolution No. \_\_\_\_\_

**Board of Supervisors, County of San Mateo, State of California**

\* \* \* \* \*

**Resolution Rescinding Previously Adopted Resolution No. 64821 for  
Pescadero Creek Road Slides Repair – Loma Mar Area**

---

**RESOLVED**, by the Board of Supervisors of the County of San Mateo, State of California, that

**WHEREAS**, this Board adopted Resolution No. 64821 on September 25, 2001, which adopted plans and specifications, determined prevailing wage scales, and called for sealed proposals for Pescadero Creek Road Slides Repair; and

**WHEREAS**, a request for a renewal of the Department of Fish and Game permit for the work was granted with an expiration date of December 31, 2002; and

**WHEREAS**, a request for extension of the window, between October 15, 2001 and June 15, 2002, in which work would be permitted under the Department of Fish and Game was denied; and

**WHEREAS**, County will re-advertise the work in the Spring of 2002 when the work is allowed by the new timing requirements of the Department of Fish and Game; and


**WHEREAS**, this Board has considered the recommendation of the Director of Public Works:

**NOW, THEREFORE, IT IS HEREBY DETERMINED AND ORDERED** as follows:

1. Resolution No. 64821, adopting plans and specifications, determining prevailing wage scales, and calling for sealed proposals for Pescadero Creek Road Slides Repair, be rescinded.

\*\*\*\*\*



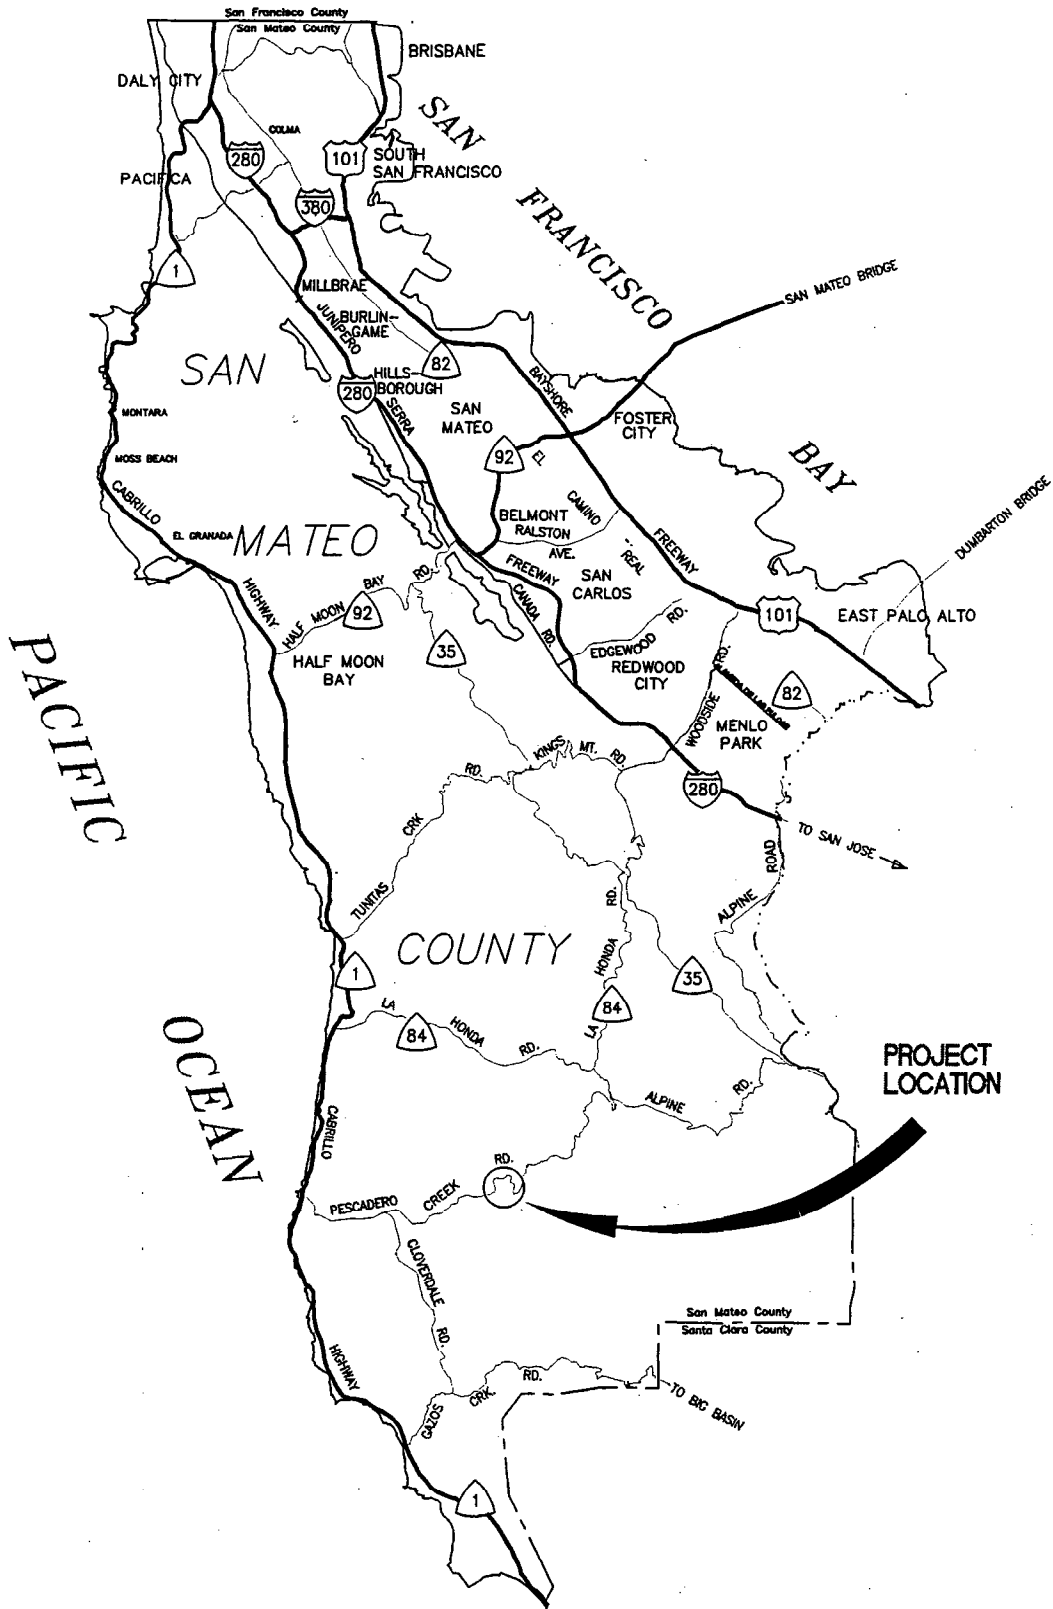

DESIGNED BY: RL  
 CHECKED BY: RD  
 DRAWN BY: RKL

**PESCADERO CREEK ROAD SLIDES REPAIR PROJECT  
 IN LOMA MAR AREA OF SAN MATEO COUNTY  
 VICINITY MAP  
 EXHIBIT "A"**

SCALE: NONE  
 DATE: 7/1/01  
 FILE NO: E4558

NEIL R. CULLEN, DIRECTOR OF PUBLIC WORKS  
 SAN MATEO COUNTY

555 COUNTY CENTER, 5TH FLOOR  
 REDWOOD CITY, CALIFORNIA 94063-1665
